



ST. CHARLES
SINCE 1834

AGENDA ITEM EXECUTIVE SUMMARY

Title: Main Street/IL Route 64 Projects – Information Only

Presenter: James Bernahl

Please check appropriate box:

<input type="checkbox"/>	Government Operations	<input checked="" type="checkbox"/>	Government Services – 10.24.11
<input type="checkbox"/>	Planning & Development	<input type="checkbox"/>	City Council

Estimated Cost:		Budgeted:	YES	<input type="checkbox"/>	NO	<input type="checkbox"/>
-----------------	--	-----------	-----	--------------------------	----	--------------------------

If NO, please explain how item will be funded:

Executive Summary:

The following presentation will provide the most up to date information to the City Council relative to the following IL Route 64 Projects:

1. IL Route 64 and Oak Street Intersection Improvements

On September 29, 2010 the City received final approval from IDOT to proceed with work within the IL 64 corridor. This work has been delayed due to the finalization of land acquisition between IDOT and the U.S. Post Office for properties within this corridor. Once notice was given to the City to proceed staff arranged a pre-construction meeting with the Contractor, Curran Paving, who was awarded the contract for construction activities on April 2, 2011, to begin mobilization to the site. Based on conversations with the Contractor, the excessive delays due to the land acquisition by the U.S. Post Office, and the potential to not have the roadway installed prior to winter conditions staff is recommending that we postpone the construction work until May 2012. Curran Paving has agreed to hold their current pricing for this contract and the revised start date.

2. IL Route 64 - (7th to Kirk Road) Project.

All work within this corridor has been completed by the City’s contractor. All traffic barricades and signage will be removed by the Contractor. The Contractor will be responsible for maintaining the temporary patching throughout the winter months. All off-site water main work and roadway repairs will be completed by November 15, 2011. The current bid date for the IDOT construction projects has been confirmed to be in January 2012.

3. IL Route 64 – (Kautz Road to Route 59) Project

- a. Up to date information to be provided at meeting.

Note: Because the IL 64 roadway projects will have no further activities taking place until spring of 2012 staff will be postponing the IL Route 64 monthly update agenda items until just prior to work commencing.

Attachments: (please list)

No Attachments


Recommendation / Suggested Action (briefly explain):

Presentation is for informational purposes only

For office use only:

Agenda Item Number: 3.a

ID	Task Name	Duration	Start	Finish
1	Prestage	83 days	Mon 1/2/12	Thu 5/3/12
2	Electrical Submittal Approval	6 days	Mon 1/2/12	Mon 1/9/12
3	Electrical Equipment Production	60 days	Mon 1/9/12	Sun 4/1/12
4	Stage 1 Temporary Pavement Markings and Traffic Control	2 days	Mon 4/16/12	Tue 4/17/12
5	Erosion Control	2 days	Wed 4/18/12	Thu 4/19/12
6	Storm Sewer	10 days	Fri 4/20/12	Thu 5/3/12
7	Stage One	25 days	Fri 5/4/12	Thu 6/7/12
8	Stage 2 Temporary Pavement Markings and Traffic Control	2 days	Fri 5/4/12	Mon 5/7/12
9	Excavation and Removals	10 days	Tue 5/8/12	Mon 5/21/12
10	Aggregate Subgrade	3 days	Tue 5/22/12	Thu 5/24/12
11	Concrete Work	4 days	Fri 5/25/12	Wed 5/30/12
12	Place Bit Binder Course	2 days	Thu 5/31/12	Fri 6/1/12
13	Furnish Topsoil and Sod/ Seed	4 days	Mon 6/4/12	Thu 6/7/12
14	Electrical Work	19 days	Fri 6/4/12	Wed 6/20/12
15	Stage Two	25 days	Thu 6/14/12	Wed 7/4/12
16	Stage 3 Temporary Pavement Markings and Traffic Control	2 days	Thu 6/14/12	Fri 6/15/12
17	Excavation and Removals	10 days	Mon 6/18/12	Fri 6/29/12
18	Aggregate Subgrade	3 days	Mon 6/18/12	Wed 6/20/12
19	Concrete Work	4 days	Thu 6/21/12	Tue 6/26/12
20	Place Bit Binder Course	2 days	Wed 6/27/12	Thu 6/28/12
21	Furnish Topsoil and Sod/ Seed	4 days	Fri 6/29/12	Wed 7/4/12
22	Electrical Work	18 days	Thu 6/30/12	Tue 7/3/12
23	Stage Three	12 days	Wed 7/4/12	Fri 7/20/12
24	Pavement Surface Removal	1 day	Thu 7/5/12	Thu 7/5/12
25	Place Surface Course	3 days	Fri 7/6/12	Tue 7/10/12
26	Final Pavement Marking	3 days	Wed 7/11/12	Fri 7/13/12
27	Electrical Work	12 days	Wed 7/11/12	Fri 7/20/12

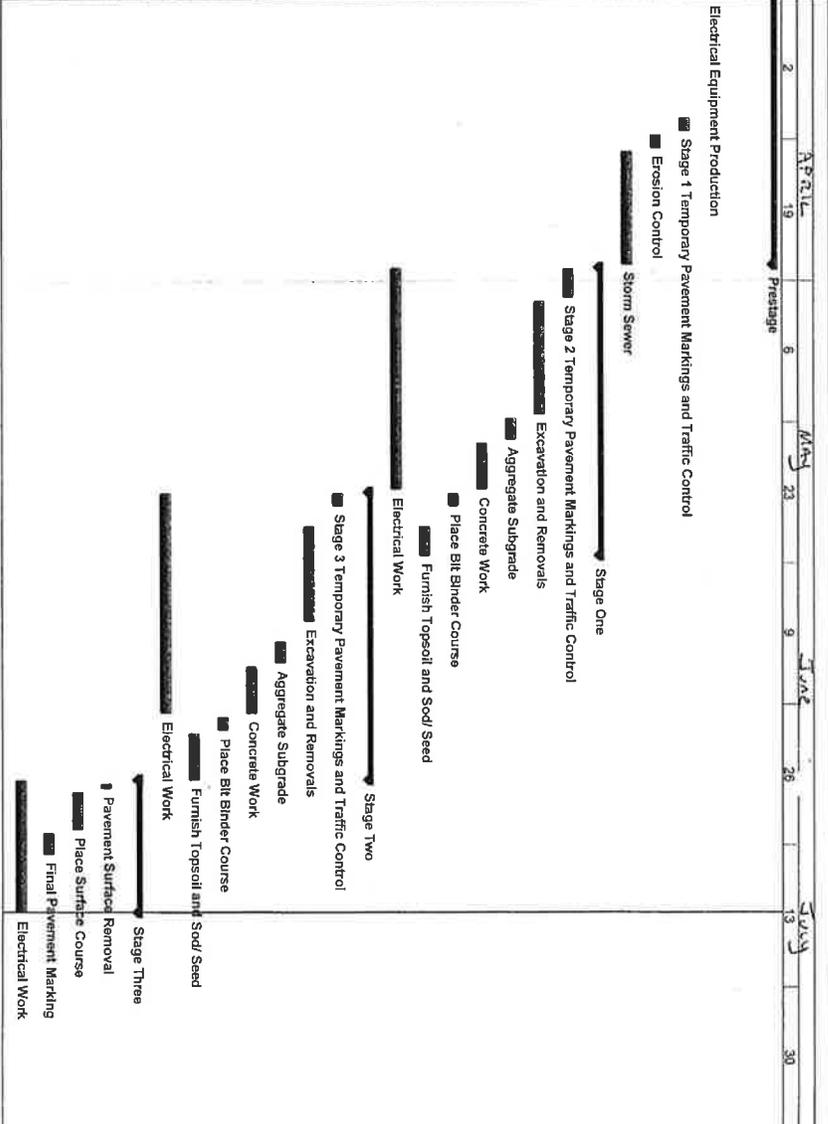

Contractor _____ Date _____
 District Construction Engineer _____ Date _____



DEKALB OFFICE / PLANT:

2220 County Farm Road ■ DeKalb, IL 60115 ■ 815.758.8113 ■ Fax 815.758.0929

Hampton, Lenzini and Renwick
380 Shepard Drive
Elgin, IL 60123
Attn: Mr. Doug Paulus

October 6, 2011

Re: City of St. Charles
Rt 64 & Oak Street Intersection Improvement


Gentlemen:

As discussed we submit the following information regarding the above mentioned project. Due to the fact that the permits and ROW were not obtained until recently Curran Contracting is willing to begin work on this project in the spring of 2012. Attached to this letter is a revised project schedule showing a revised completion date of 7/20/2012.

This work will be completed by Curran Contracting at the original contract unit prices with no cost increase to the City of St. Charles.

Please review the attached progress schedule and let us know if this acceptable to the City of St. Charles.

Very Truly Yours,



David Schmoer
Project Manager Curran Contracting
